

NYADI PHIDI HYDROPOWER PROJECT (21.4 MW)

MONTHLY PROGRESS REPORT



Construction of Nyadi Phidi Hydropower Project (21.4 MW)

Prepared By:

North Summit Hydro Ltd.

Babarmahal, Kathmandu



JUNE 2026

General Information

Project Name	Nyadi Phidi Hydropower Project (21.4 MW)
Project Number	
Client's Name	North Summit Hydropower Limited
Report	Monthly Progress Report
Remarks	

Preparation, Review and Authorization

Date	Prepared by	Reviewed by	Approved for Issue by
8 th July 2026	Sangam Malla	Niroj Phuyal	

Issue Register

Distribution List	Date Issued	Number of Copies
NS Hydro		
NS Hydro Staff		
NPHPP Board		
Misc.		

Institutional Arrangement

Client	North Summit Hydro Limited
Design Consultant	Hydro-Consult Engineering Limited (HCE) and Innovative Engineering Services Pvt. Ltd (IES) JV
Civil Contractor	Kalika-SAI-Karna JV
HM Contractor	Machchhapuchhre Metals and Machinery Pvt. Ltd.
EM Contractor	Flovel Energy Pvt. Ltd.



Executive Summary

The Nyadi-Phidi Hydropower Project, being developed by North Summit Hydro Limited is located in Lamjung District of Gandaki Province. The project will utilize the perennial flow of the Nyadi River for power generation. The project has secured major statutory approvals including the grid connection agreement, power purchase agreement and generation license, and has achieved financial closure. The contracts for the **civil works, hydromechanical works and electromechanical works** have been awarded to **Kalika-SAI-Karna JV, Machhapuchhre Metal and Machinery Works Pvt. Ltd. and Flovel Energy Pvt. Ltd.**, respectively.

This report presents an overview of the construction activities carried out at the project site. Works across various project components are progressing in line with the planned schedule. At the **Intake Area**, site clearance has been completed and the first-stage river diversion for cofferdam construction has been successfully carried out. Following the river diversion, concreting works for the undersluice structure have commenced with the raft concrete for the first and second panels already completed. In the **Desander Area**, site clearance has been completed and excavation has reached Elevation 2948 masl, corresponding to the top level of the hopper.

At the **Headrace Tunnel**, inlet portal excavation has been completed and the necessary labor camp facilities have been established. Tunnel excavation is currently in progress, with 59.2 m completed to date. The **Penstock Tunnel** excavation, totaling **253 m** including the required widening for the vertical shaft has been completed. 228.45 m of the **Vertical Shaft** excavation has been complete. Along the **Penstock Alignment**, excavation from Anchor Block (AB) 8 to AB 12 has been completed and the foundation excavation and first lift concreting for Anchor Block 9 and 12 have also been completed.

For the **Hydromechanical Works**, site workshop and camp facility have been completed. Fabrication of steel penstock pipe has been continued at Pokhara Shop. In total, 427 nos of variable sizes (2.5 m each) pipe and six bends from AB 7 to AB 12 have been transported to site workshop and welding of 284 nos of variable size (2.5m each) and AB 9 and AB 12 bends have been completed and welding works are currently in progress at the site.

Regarding the **Ropeway** system, the erection of all three towers have been completed. The main track rope and pulling rope have been shifted from the base station to Top anchor point and rope tensioning is also completed. **Construction Power** has been successfully extended to both the Headworks and Powerhouse area. The **Access Road** leading to the Headworks has been completed and the access road towards the Powerhouse has been constructed up to the top level of the powerhouse area.

For the **Bailey Bridge Structure**, the bridge was not feasible in previous alignment due to continuous mass falling, so excavation of the both abutments has been completed in new alignment and the concreting works and rubble masonry work for protection wall on both abutments have been completed. In addition, the **Army Camp** infrastructure, including the superstructure and bunker facilities has been completed.



Overall, the project construction activities are progressing steadily across multiple fronts, with several key preparatory and structural works already completed and subsequent construction stages being actively pursued.



TABLE OF CONTENTS

1	Introduction	1
1.1	Project Description.....	1
1.2	Accessibility to Project Site.....	1
1.3	Salient Features of the Project.....	1
2	Resources and Facilities.....	6
2.1	Resources from Client.....	6
2.1.1	Human Resources.....	6
2.1.2	Facilities.....	6
2.2	Explosive	7
2.3	Resources from Contractor.....	7
2.3.1	Human Resources.....	7
2.3.2	Equipment.....	8
2.3.3	Material.....	9
3	Activities at Site in June 2026.....	10
3.1	Infrastructure Development.....	10
3.1.1	Internal Approach Road.....	10
3.1.2	Bridge	10
3.1.3	Ropeway Construction	10
3.1.4	Construction Power	10
3.2	Civil Works	10
3.2.1	Penstock Tunnel and Vertical Shaft Construction	11
3.2.2	Penstock Alignment	11
3.2.3	Headworks	11
3.2.4	Inlet HRT	11
3.3	Hydromechanical Works.....	11
3.4	Electromechanical Works.....	12
3.5	Transmission Line Works	12
3.6	Other Works	12
3.6.1	Laboratory Setup.....	12
3.6.2	Health and Safety	12
3.6.3	Quality Control	12
3.6.4	Regular Meeting.....	12

3.7	Project Progress	13
4	Expected Progress for July 2026	15
4.1	Internal approach to Powerhouse.....	15
4.2	Bridge	15
4.3	Ropeway Construction	15
4.4	Headworks	15
4.5	Inlet HRT.....	15
4.6	Penstock Tunnel Construction.....	15
4.7	Hydromechanical works.....	15
4.8	Penstock Alignment	15
5	Appendices	16
5.1	Appendix 1: Photographs	16



LIST OF FIGURES

Figure 1: Rebar work in Undersluice gated panel in Headworks	16
Figure 2: Rebar and formworks in Undersluice gated panel in Headworks.....	16
Figure 3: Undersluice gated panel after raft concreting	17
Figure 4: Inlet tunnel face at ch 0+053.60m.....	17
Figure 5: Face drilling in Inlet tunnel at ch 0+056.10m	18
Figure 6: Rib installation work in Inlet tunnel.....	18
Figure 7: Preparation for drilling in Vertical shaft tunnel.....	19
Figure 8: Bend and straight pipe erection completed in AB 12	19
Figure 9: 1 st lift plum concreting in AB 9	20
Figure 10: Stem wall along with RRM of bridge right abutment.....	20
Figure 11: Bridge right abutment after removal of formwork.....	21
Figure 12: Concreting in Bridge left abutment stem wall	21
Figure 13: Preparation of AB 9 bend in HM workshop	22
Figure 14: Powerhouse area after blasting	22
Figure 15: Drilling work for excavation in Powerhouse area	23
Figure 16: Rope tensioning of Ropeway	23
Figure 17: Soil resistivity test of Transmission line	24

LIST OF TABLES

Table 1: Salient features of the project.....	1
Table 2: Human resources of Client	6
Table 3: Facilities of Client	6
Table 4: Stock of Blasting materials	7
Table 5: Human Resources of Civil Contractor	7
Table 6: Human Resources of HM Contractor	8
Table 7: Equipment of Civil Contractor.....	8
Table 8: Equipment of HM Contractor	9
Table 9: Material Stock of Civil Contractor.....	9

1 Introduction

1.1 Project Description

Nyadi-Phidi Hydropower Project (NPHPP) is located in Lamjung district of Gandaki Province. The project site is located in Marshyangdi Rural Municipality. Geographically, the project area is located in between latitudes 28°24'27" - 28°26'12" N and longitudes 84°30'10" - 84°31'43" E.

The project site can be reached from Kathmandu via a 189 km paved road to Besisahar, the district headquarters of Lamjung. From Besisahar, the site is approximately 52 km further, mostly along an earthen road.

The hydropower scheme includes a 15m length boulder lined weir with a crest elevation of 2950.6 masl. The intake is located on Nyadi River near Jaluchhe village at an elevation of 2950.1 masl, capturing flow from a catchment area of 54.03 km². The project utilizes flow of Nyadi and two downstream Kholsis during dry months and the head created by tunnel and penstock between headworks and powerhouse site to generate power.

1.2 Accessibility to Project Site

The Project site is accessible from Kathmandu by a 189 km long asphalt road up to Besisahar, the district headquarters of Lamjung. The site is approximately 52 Km from Besisahar. The access road follows the alignment through Naiche, Kafaldada, and Dahare before reaching the project location. Besisahar is the nearest town to the site, while the closest Indo-Nepal border point is Raxaul.

Kathmandu – Besisahar – Nyadi – Thulibeshi – Naiche- Kafaldanda – Dahare- Project Site

1.3 Salient Features of the Project

The salient features of the project are presented in Table 1.

Table 1: Salient features of the project

S. N	Description	Detail Design Report
1	Project Location	
	Province	Gandaki Province
	District	Lamjung
	Intake Site	Jaluchhe Village, Marsyangdi Rural Municipality, Ward No-7
	Powerhouse Site	Confluence of Nyadi and Phidi River, Marshyangdi Rural Municipality, Ward no. 7
	Geographical Co-ordinates	
	Latitude	28° 24' 27" N- 28° 26' 12" N
	Longitude	84° 30' 10" E- 84° 31' 43" E
2	General	
	Name of River	Nyadi River



S. N	Description	Detail Design Report
	Nearest Town	Besisahar
	Type of Scheme	Run-of-River
	Gross Head	690.10 m
	Head loss at Design Discharge	10.18 m
	Net Head at Design Discharge	679.92 m
	Installed Capacity	21.40 MW
	Average Annual Energy after Outage	122.94 GWh
3	Hydrology	
	Catchment Area (Nyadi)	54.03 Km ²
	Mean Annual Discharge (Nyadi)	4.66 m ³ /sec
	Design Discharge	3.60 m ³ /sec
	Riparian Release (Nyadi River)	0.11 m ³ /sec
	Design Flood Discharge (100 years flood)	123.45 m ³ /sec at Intake site
	Design Flood Discharge (100 years flood)	188.42 m ³ /sec at Powerhouse site
	Average Annual Precipitation	3316 mm
4	Diversion Weir & Undersluice	
	Type of Weir	Boulder Lined Weir
	Length of Weir	15 m
	Crest Elevation	2950.60 masl
	Spillway type	Free overflow
	Undersluice Opening (W X H)	2.50 m x 2.50 m
	Undersluice Invert Level	2946.49 masl
5	Trash passage	
	Size of trash passage (W x H)	1.5 m x 2.5 m
	Invert level of opening	2950.10 masl
	Length of trash passage	12.0 m
6	Intake and Gravel Trap	
	Type of Intake	Side Intake-Submerged orifice type
	No. of Openings	2 nos.
	Size of Intake (W x H)	2.0 m x 1.6 m
	Intake Sill Level	El. 2950.10 masl
	Intake Invert Level	El. 2948.50 masl
	Length of Gravel Trap	4.0 m
	Width of Gravel Trap	4.8 m
	Particle size to be trapped	5 mm
	Flushing Orifice size (W x H)	0.8 m x 0.8 m
	Flushing Culvert size (W x H)	0.8 m x 1.0 m

S. N	Description	Detail Design Report
7	Approach Culvert	
	Type	RCC Culvert
	No. of culverts	1 no.
	Length	105.0 m
	Bed slope	1 in 400
	Size (W x H)	1.6 m x 1.5 m
8	Approach Culvert (Diverged)	
	Type	RCC Culvert
	No. of culverts	2
	Length of each culvert	25.0 m
	Bed slope	1 in 600
	Size (W x H)	1.1 m x 1.5 m
9	Settling Basin	
	Type	Concrete, Double Bay Dufour
	Dimension (L x B x H)	35.0 m x 6.5 m x 4.1 m
	Inlet Transition Length	12.70 m
	Particle Size to be settled	0.15 mm
	Trapping Efficiency	80% (Vetter's Method)-100 % (Camp's method)
	Sediment Flushing Orifice size (W x H)	1.0 m x 1.2 m
10	Headrace culvert	
	Type	RCC box
	Culvert size (W x H)	2.2 m x 2.2 m
	Length	59.5 m
11	Headrace Tunnel	
	Type	Inverted D-shaped
	Excavation Size (W x H)	2.5 m x 2.9 m
	Minimum Finished Size (W x H)	2.2 m x 2.5 m
	Length	2020 m
	Type of Lining	Shotcrete/concrete lined as per rock class
12	Surge Shaft	
	Type	Simple Cylindrical
	Total Height	25 m
	Finished Diameter	4.5 m
	Up Surge Level	2956.73 masl
	Down Surge Level	2941.88 masl
	Normal Operation Level	2950.60 masl
13	Drop Shaft	

S. N	Description	Detail Design Report
	Type / Pipe Material	Circular / Steel pipe
	Internal Diameter-Steel Pipe	1.2 m
	Minimum Finished Diameter	2.2 m
	Excavation Diameter	2.4 m
	Backfill Concrete (M15 Self compacting concrete)	50 cm (Varying)
	Length	255 m
14	Penstock Tunnel	
	Type	Inverted D-shaped
	Excavation Size (W x H)	2.9 m x 3.1 m
	Length	253 m
	Type of Lining	Shotcrete/concrete lined as per rock class
15	Steel Penstock Pipe	
	Type	Steel Pipe
	Internal Diameter	1.2 m
	Length (Before bifurcation)	1490 m
	Diameter-Length (After bifurcation)	0.85 m dia. of 15 m each
	Steel Thickness	8 mm to 40 mm (IS 2062 E350B0 or Equivalent)
16	Powerhouse	
	Type	Surface
	Size (L x W)	28.85 m x 19.50 m
	Height	14.65 m
	Powerhouse Machine Floor Level	El. 2259.00 masl
17	17 Tailrace Culvert	
	Type	RCC Box
	Size (W x H)	1.50 m x 1.50 m
	Maximum Tailwater Level (Considering 10% COL)	2256.78 masl
	Minimum Tailwater Level (Considering 20% of design discharge on each unit)	2256.31 masl
	Tailrace Water Level	NA
18	Turbine	
	Type	Pelton-Horizontal Axis
	Number	2 nos.
	Rated Output Capacity per unit	11.05 MW + 10 % COL
	Turbine Axis Level	2260.50 masl
	Net Head	679.92 m
	Discharge per Unit	1.8 m ³ /sec

S. N	Description	Detail Design Report
	Efficiency	91.5%
19	Governor	
	Type	Digital Electronic Governor with PID
	Adjustment for Speed Drop	Up to 10 %
20	Generator	
	Type	Three phases, Synchronous
	Rated Output Capacity per Unit	12.60 MVA + 10 % COL
	Power Factor	0.85
	Voltage	11 kV
	Frequency	50 Hz
	No of Units	2 nos.
	Excitation System	Brushless Excitation
	Efficiency	97.5%
21	Transformer	
	Type	Three phase-Oil Immersed, Outdoor
	Rated Capacity	13.9 MVA
	Voltage Ratio	132/11 kV
	No of Units	2 nos
	Vector Group	YNd11
	Efficiency	99%
22	Transmission Line	
	Voltage level	132 kV
	Length	13.5 Km
	Conductor Type	BEAR
	From	Nyad- Phidi HPP's Switchyard
	To	Nyadi HPP'S Switchyard (Connection Point)
23	Access Road	
	Naiche to Kharka (Zero Point)	15 Km
	Kharka to Powerhouse	11 Km

2 Resources and Facilities

The project is supported by essential resources and facilities required for its successful implementation. Key infrastructure including access roads and communication systems is in place. Necessary construction equipment, materials and storage areas are being arranged near the site, with provisions for worker accommodations and site offices. Detailed information regarding the available resources and supporting facilities is presented in the sections below.

2.1 Resources from Client

The resources provided by the client under various categories are described below.

2.1.1 Human Resources

Human resources available are listed below.

Table 2: Human resources of Client

S. N	Designation	Nos	Remarks
1	Resident Engineer	1	
2	Sr. Mechanical Engineer	1	
3	Project Engineer	1	
4	Civil Engineer	1	
5	Geologist	1	
6	Sub Engineer	1	
7	Site Supervisor	1	
8	Electrical Sub Engineer	1	
9	Surveyor	1	
10	Driver	2	
11	Cook	1	

2.1.2 Facilities

The facilities of the client are listed in the table below.

Table 3: Facilities of Client

S. N	Description	Nos	Remarks
1	Vehicle	3	
2	Motor bike	1	
3	Excavator	1	
4	Petrol Generator	1	
5	Diesel Generator	1	
6	Total Station	2	
7	Computer set	1	

8	Printer	2	
9	Office building	1	
10	Staff quarter	2	
11	Guest house	1	
12	Kitchen building	1	

2.2 Explosive

Table 4: Stock of Blasting materials

S. N	Description	Unit	Quantity	Remarks
1	Emulsion	Kg	17302.3	Remaining
2	Electric Detonator	Nos	26142	
3	Non-Electric Detonator	Nos	6173	
4	Deto- Cord	M	6417	

2.3 Resources from Contractor

2.3.1 Human Resources

Human resources available are listed below

Table 5: Human Resources of Civil Contractor

S. N	Designation	Nos	Remarks
1	Project Manager	1	
2	Site In-charge	1	
3	Engineer	4	
4	Geologist	1	
5	Accountant	1	
6	Surveyor	3	
7	Lab Technician	1	
8	Supervisor	5	
9	Blaster	2	
10	Electrician	3	
11	Welder	3	
12	Mechanic	1	
13	Carpenter/Plumber	3	
13	Driller	1	
14	Driller's helper	2	
15	Driver	9	
16	Operator	7	
17	Helper	4	

18	Cook	3	
19	Vertical Shaft manpower	12	
20	Penstock Alignment manpower	7	
21	HRT Inlet Manpower	20	
22	Ropeway manpower	8	
23	Bridge Manpower	7	
24	Headworks Manpower	12	

Table 6: Human Resources of HM Contractor

S. N	Designation	Nos	Remarks
1	Site Engineer	1	
2	Supervisor	0	
3	Site Supervisor	1	
4	Excavator Operator	1	
5	Driver	1	
6	Welder	6	
7	Fitter	1	
8	Grinder	1	
9	Helper	1	
10	Store Keeper	1	
11	QC Technician	1	
12	Electrician	1	
13	Sand blasting team	5	
14	Cook	1	

2.3.2 Equipment

The equipments of the contractor are listed in the table below.

Table 7: Equipment of Civil Contractor

S. N	Description	Nos	Remarks
1	Excavator	5	
2	JCB Backhoe Loader	2	
3	6-Wheeler Tipper	2	
4	10-Wheeler Tipper	0	
5	Tractor	3	
6	Bolero	5	
7	Motorcycle	2	
8	Diesel Generator	5	
9	Bar bending machine	2	

10	Compressor	6	
11	Shotcrete Machine	2	
12	Grouting Machine	1	
13	Water Pump	3	
14	Welding Machine	2	
15	Jack Hammer	10	
16	Chainsaw Machine	2	
17	Muck Loader	1	
18	Batching plant	1	
19	Transit Mixture	1	
20	Loader	1	
21	Monkey Jumper	1	
22	Self-loading Mixture	2	

Table 8: Equipment of HM Contractor

S. N	Description	Nos	Remarks
1	Excavator	1	
2	Welding Machine	9	
3	Tractor	1	
4	Compressor	1	
5	Diesel Generator	1	

2.3.3 Material

Table 9: Material Stock of Civil Contractor

S. N	Description	Unit	Quantity	Remarks
1	Diesel	Ltr	10000	
2	Cement	Bag	2200	

3 Activities at Site in June 2026

Activities carried out during this period are briefly described hereunder:

3.1 Infrastructure Development

For the success of the project, most of the required infrastructures are been constructed and few are been ongoing.

3.1.1 Internal Approach Road

To Headworks:

Towards the headworks, internal approach road has been completed. 5+100.00m of the road which equals to almost 100 % of the total road is completed and widening and upgrading of the road is also completed.

To Powerhouse:

No work in this month. Upto the date, excavation of the internal approach road to powerhouse is completed up to 0+680 m chainage and about 220 m of the road section is remaining for excavation.

3.1.2 Bridge

The civil superstructure works for both bridge abutments were completed during this month. Construction of the wing walls for the protection of the main bridge structure is currently underway

3.1.3 Ropeway Construction

All the equipment for the construction of the ropeway has arrived at the project site. The accessories for tower erection have been shifted to all respective towers from the base location. The construction of the all three towers have been completed and the main track rope and pulling rope have been shifted from base location to the top anchor. The tensioning of rope has been completed and the transportation of winch has been halted due to settlement observed in the top anchor.

3.1.4 Construction Power

Construction power from NEA has been made available at the project site. Construction power of NEA is being supplied to both headworks and powerhouse areas.

3.2 Civil Works

The civil works of this project involve the construction of key infrastructure components such as the headworks, diversion weir, intake, approach culvert, settling basin, headrace tunnel, surge shaft, penstock alignment and powerhouse. These works are essential for guiding and controlling the flow of water to generate electricity efficiently. Activities under the civil works include excavation, concreting, tunnelling, slope stabilization and construction of hydraulic structures.

3.2.1 Penstock Tunnel and Vertical Shaft Construction

The penstock tunnel is a component that conveys pressurized water through penstock pipe from surge shaft to the powerhouse turbines. The tunnel alignment is carefully selected to minimize hydraulic losses while ensuring structural stability. The penstock tunnel and vertical shaft have a total designed length of 253 meters and 255 meters.

Excavation of the Penstock Tunnel has been completed and the widening of the tunnel for raise climber is also completed. The excavation is being carried out with a strong emphasis on ensuring safety and maintaining structural integrity throughout the process. The excavation of 67.1m of the vertical shaft has been completed this month, bringing the total excavated length to 228.45m up to this month.

3.2.2 Penstock Alignment

The site clearance and excavation for track opening from AB 9 to AB 12 have been completed and excavation for AB 9 and AB 12 is also completed. The plum concrete work in AB 9 and AB 12 have been started. The erection of AB 12 bend has been completed and the erection of AB 9 has also commenced.

3.2.3 Headworks

In Headworks area, site clearance in intake area and layout of different structures is completed. The first-stage river diversion for cofferdam construction has been completed. The concreting works in raft of both undersluice u/s panel and undersluice gated panel have been completed. Also, in Desander area, site clearance works have been completed and 60 percent of excavation have been completed.

3.2.4 Inlet HRT

Camp construction works for sub-contractor is completed and portal preparation works have been completed. 59.2m excavation of headrace tunnel have been completed up to this month and excavation work is on progress.

3.3 Hydromechanical Works

The hydromechanical works for the project are progressing now. A total of 208 steel plates, equivalent to approximately 1,180 tons have been arrived and stored at the mechanical yard in Pokhara for further fabrication and assembly. These materials are a key component for the hydromechanical works, including penstock and associated structures. The construction of three staff camps at the project site to accommodate personnel for the ongoing and upcoming works has been completed.

A team from the hydromechanical contractor has been mobilized to the site, the construction of the workshop is completed. Also, pipe transportation to the site is ongoing and 427 nos. of pipes of variable sizes and AB-7 to AB-12 bends have been transported which is almost 1082.5 m. Furthermore, welding of 284 nos of variable size (2.5m each) and AB-9, AB-12 bends have been completed and testing of 280 nos of pipes and AB-9, AB-12 bends have been completed. Welding and testing of pipes is ongoing.



3.4 Electromechanical Works

The electromechanical works for the project are in the preliminary phase. The process for selecting a qualified company for the supply and installation of electromechanical equipment has been completed which includes evaluation of proposals from potential contractors to ensure compliance with technical specifications, quality standards and project timelines. The contract has been awarded to Flovel Energy Pvt. Ltd. The selected company will be responsible for the procurement, delivery, installation, testing and commissioning of key components such as turbines, generators, control systems and auxiliary equipment essential for the successful operation of the hydropower plant. The design work for the manufacturing of electromechanical equipment is currently in progress.

3.5 Transmission Line Works

For the transmission line works, the Initial Environmental Examination (IEE) has been completed and the survey license has been obtained. The detail design of foundation and tower body is in process.

3.6 Other Works

3.6.1 Laboratory Setup

The construction of the on-site laboratory and the installation of the Los Angeles Abrasion testing machine and the Compressive Strength testing machine (CTM) has been completed. The calibration of CTM has been also completed and the mix design process have been completed.

3.6.2 Health and Safety

Health and safety measures have been implemented to ensure the safe execution of project activities. Personal Protective Equipment (PPE) has been provided to all the staff and workers in road construction and tunnel excavation and its use is strictly enforced on site. Additionally, instruction signboards have been installed at both the construction and project areas to promote awareness and compliance with safety protocols.

3.6.3 Quality Control

Quality control at the project site is being closely monitored to ensure all construction activities meet the required standards. Site engineer and supervisor are observing the quality of work on a regular basis, with particular attention to material handling and workmanship. Material testing is planned to commence as soon as the on-site laboratory setup is completed and the testing machines are properly calibrated. This will enable systematic verification of construction materials, further strengthening the overall quality assurance process.

3.6.4 Regular Meeting

Regular meetings are held once a week following the submission of the weekly progress report. These meetings serve as a platform to review the current status of work, discuss challenges,

and plan upcoming activities. Participation from key personnel ensures effective coordination, timely decision-making and smooth progress at the project site.

3.7 Project Progress

A summary of the project's progress is presented in the table below.

S. N.	Description	Unit	Total Qty	Till Previous Month	This Month Progress	Completed Till Date	% Completed
A	Infrastructure Development						
1	Internal Approach Road						
	To Headworks	km	5.10	5.10	0.00	5.10	100%
	To Powerhouse	km	0.90	0.68	0.00	0.68	75.56%
2	Ropeway						
	Supply and delivery of equipment and accessories	LS	1	1	0	1	100%
	Shifting of equipment and accessories	LS	1	0.95	0	0.95	95%
	Tower erection, testing and commissioning	LS	1	0.7	0	0.7	70%
3	Construction power						
	Up to Powerhouse	LS	1	1.0	0.0	1.0	100%
	Up to Headworks	LS	1	1.0	0.0	1.0	100%
4	Army Camp						
	Foundation work	LS	1	1.0	0.0	1.0	100%
	Superstructure	LS	1	1.0	0.0	1.0	100%
	Plumbing and electrical work	LS	1	1.0	0.0	1.0	100%
	Fencing and finishing work	LS	1	1.0	0.0	1.0	100%
5	Bridge						
	Excavation	LS	1	0.5	0.5	1	100%
	Superstructure	LS	1	0.1	0.4	0.5	50%
	Bailey bridge erection	LS	1	0	0	0	0%
B	Civil Work						
1	Mobilization	%	100%	100%	0%	100%	100%
	Underground works						

S. N.	Description	Un it	Total Qty	Till Previous Month	This Month Progress	Completed Till Date	% Completed						
2	Penstock tunnel	rm	253	253.75	0.0	253.75	100%						
3	Vertical Shaft Tunnel	m	255	161.35	67.10	228.45	89.59%						
4	Headrace Tunnel	m	2020	52.0	7.2	59.2	2.57%						
	Surface works												
5	Headworks												
a	River diversion works	LS	1	0.5	0	0.5	50%						
b	Undersluice												
	Excavation	LS	1	1	0	1	100%						
c	Desander												
	Excavation	LS	1	0.6	0	0.6	60%						
6	Penstock Alignment												
	Excavation CAB-8 to CAB-12	rm	0+560 to 0+800	240	0	240							
C	Hydromechanical Work												
1	Mobilization	%	100%	50%	50%	100%	100%						
2	Steel plate reached at Pokhara shop	Ton	1180	1180	0	1180	100%						
3	Fabrication of pipe		Started from 28 th Nov 2025 at Pokhara shop										
	Size (mm)	36	32	28	25	22	20	18	16	14	12	10	8
	Edge Preparation	54	132	93	18	12	12	12	18	10	7	6	53
	Rolling	54	132	93	18	12	12	12	18	10	7	6	53
	LS Welding (2.5m)	37	90	53	18	12	12	12	18	10	5	1	16
	NDT (2.5m)	36	88	46	18	11	11	12	18	10	5	1	11
	Grid blasting	34	77	35	18	11	11	12	17	10	4	1	11
	Painting	30	75	34	15	7	8	12	17	10	4	1	11
	Site Reached	54	132	93	18	12	12	12	18	10	7	6	53
D	Electromechanical Work												
1	Bid Submission	LS	1	1	0	1							
2	Contract award	LS	1	0	1	1							
E	Transmission Line Work												

S. N.	Description	Unit	Total Qty	Till Previous Month	This Month Progress	Completed Till Date	% Completed
1	Detail Design	LS	1	1	0	40%	40%

4 Expected Progress for July 2026

The work throughout the all fronts will be continued and the expected progress for the month of June is hereunder.

4.1 Internal approach to Powerhouse

Track Excavation of the internal access road to top of powerhouse is almost completed. Furthermore, layout of the powerhouse area and excavation is expected to start in the month.

4.2 Bridge

The erection of bailey bridge is expected to complete this month.

4.3 Ropeway Construction

The transportation of winch up to top station will be started after inspection of top anchor.

4.4 Headworks

In Headworks area, excavation of intake will be started and concrete works of two panel will be continued in undersluice. Also, in Desander area, excavation of desander will resume.

4.5 Inlet HRT

Tunnel excavation will be continued targeting 30 m for this month.

4.6 Penstock Tunnel Construction

Tunnel excavation will be continued targeting to breakthrough for this month.

4.7 Hydromechanical works

Hydromechanical team is transporting the fabricated pipe to site and welding works will be continued. The AB-9 bend will be erected in this month.

4.8 Penstock Alignment

The construction of AB-12 and AB-9 will be continued and the excavation in AB 10 will be started.

5 Appendices

5.1 Appendix 1: Photographs

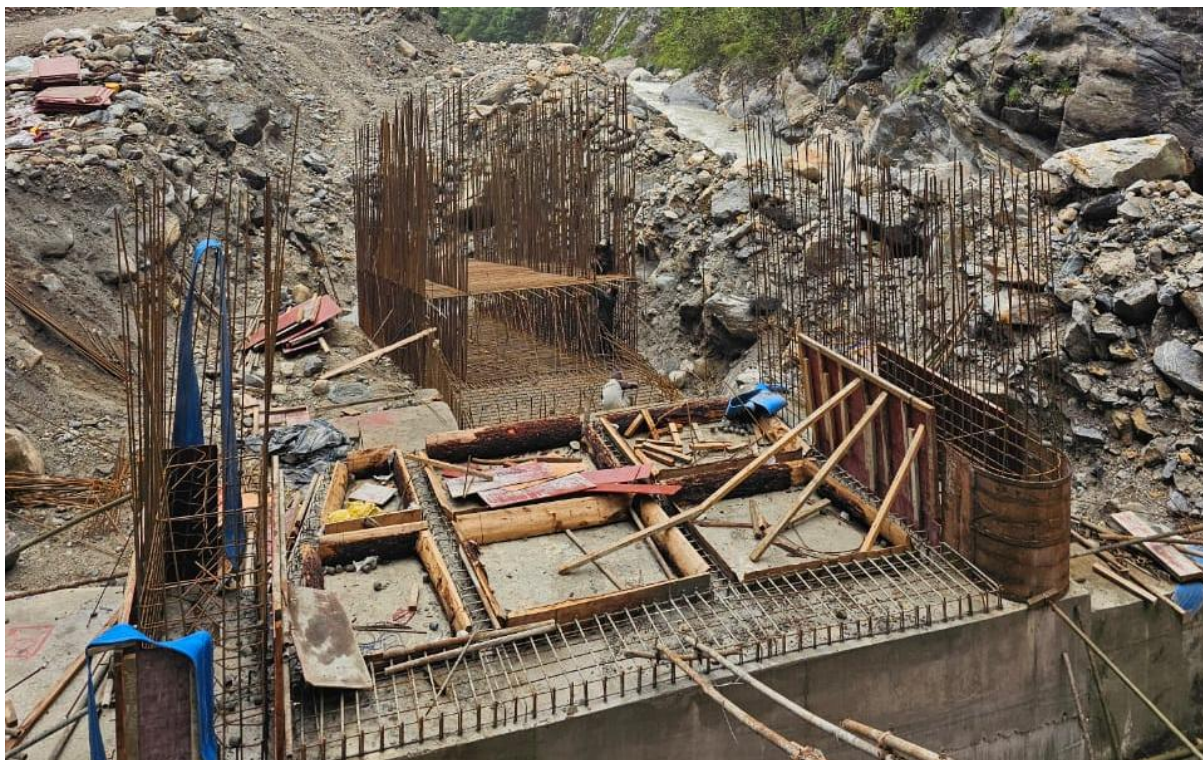


Figure 1: Rebar work in Undersluice gated panel in Headworks



Figure 2: Rebar and formworks in Undersluice gated panel in Headworks



Figure 3: Undersluice gated panel after raft concreting



Figure 4: Inlet tunnel face at ch 0+053.60m



Figure 5: Face drilling in Inlet tunnel at ch 0+056.10m



Figure 6: Rib installation work in Inlet tunnel

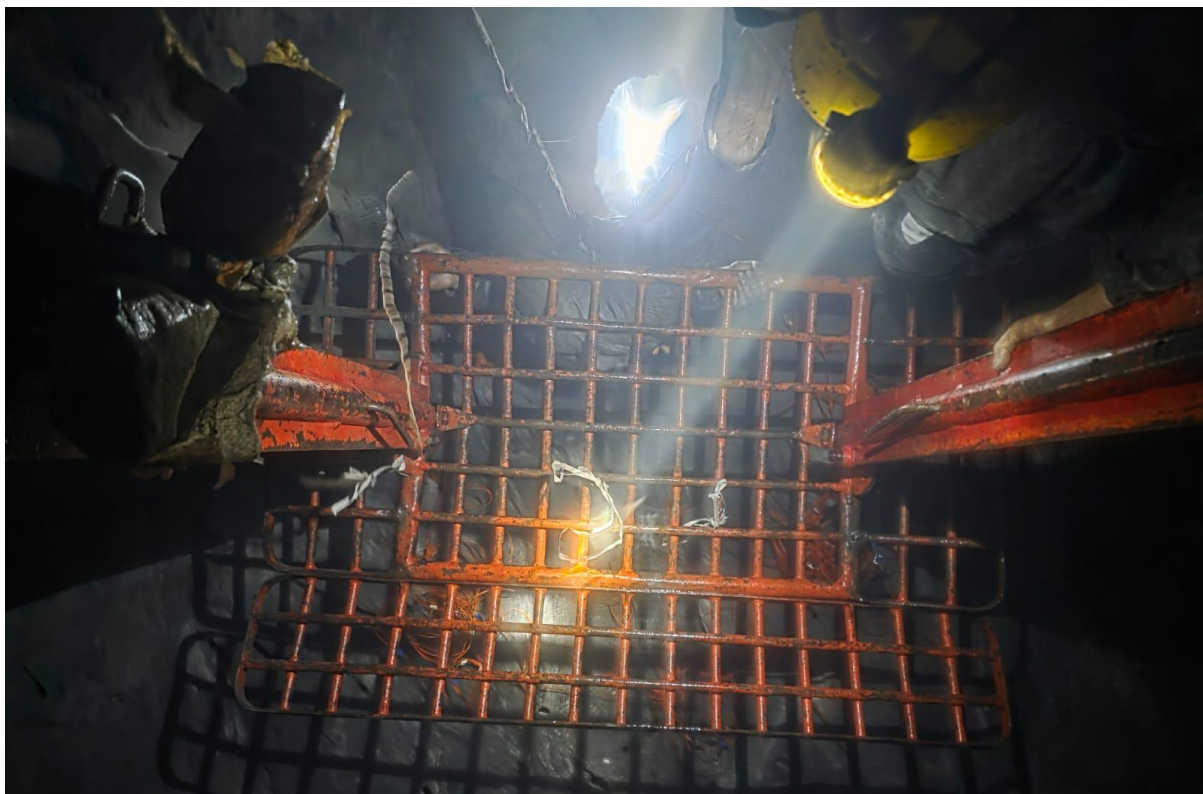


Figure 7: Preparation for drilling in Vertical shaft tunnel



Figure 8: Bend and straight pipe erection completed in AB 12



Figure 9: 1st lift plum concreting in AB 9



Figure 10: Stem wall along with RRM of bridge right abutment



Figure 11: Bridge right abutment after removal of formwork



Figure 12: Concreting in Bridge left abutment stem wall



Figure 13: Preparation of AB 9 bend in HM workshop



Figure 14: Powerhouse area after blasting



Figure 15: Drilling work for excavation in Powerhouse area



Figure 16: Rope tensioning of Ropeway



Figure 17: Soil resistivity test of Transmission line
